



CONSTRUCTION PROGRESS UPDATE

JUNE 2026



PROJECT OVERVIEW

During the month of June, we made significant progress in the excavation and shoring activities of the project. The second line of the steel strutting system is close to completion, allowing excavations to safely advance to deeper levels.

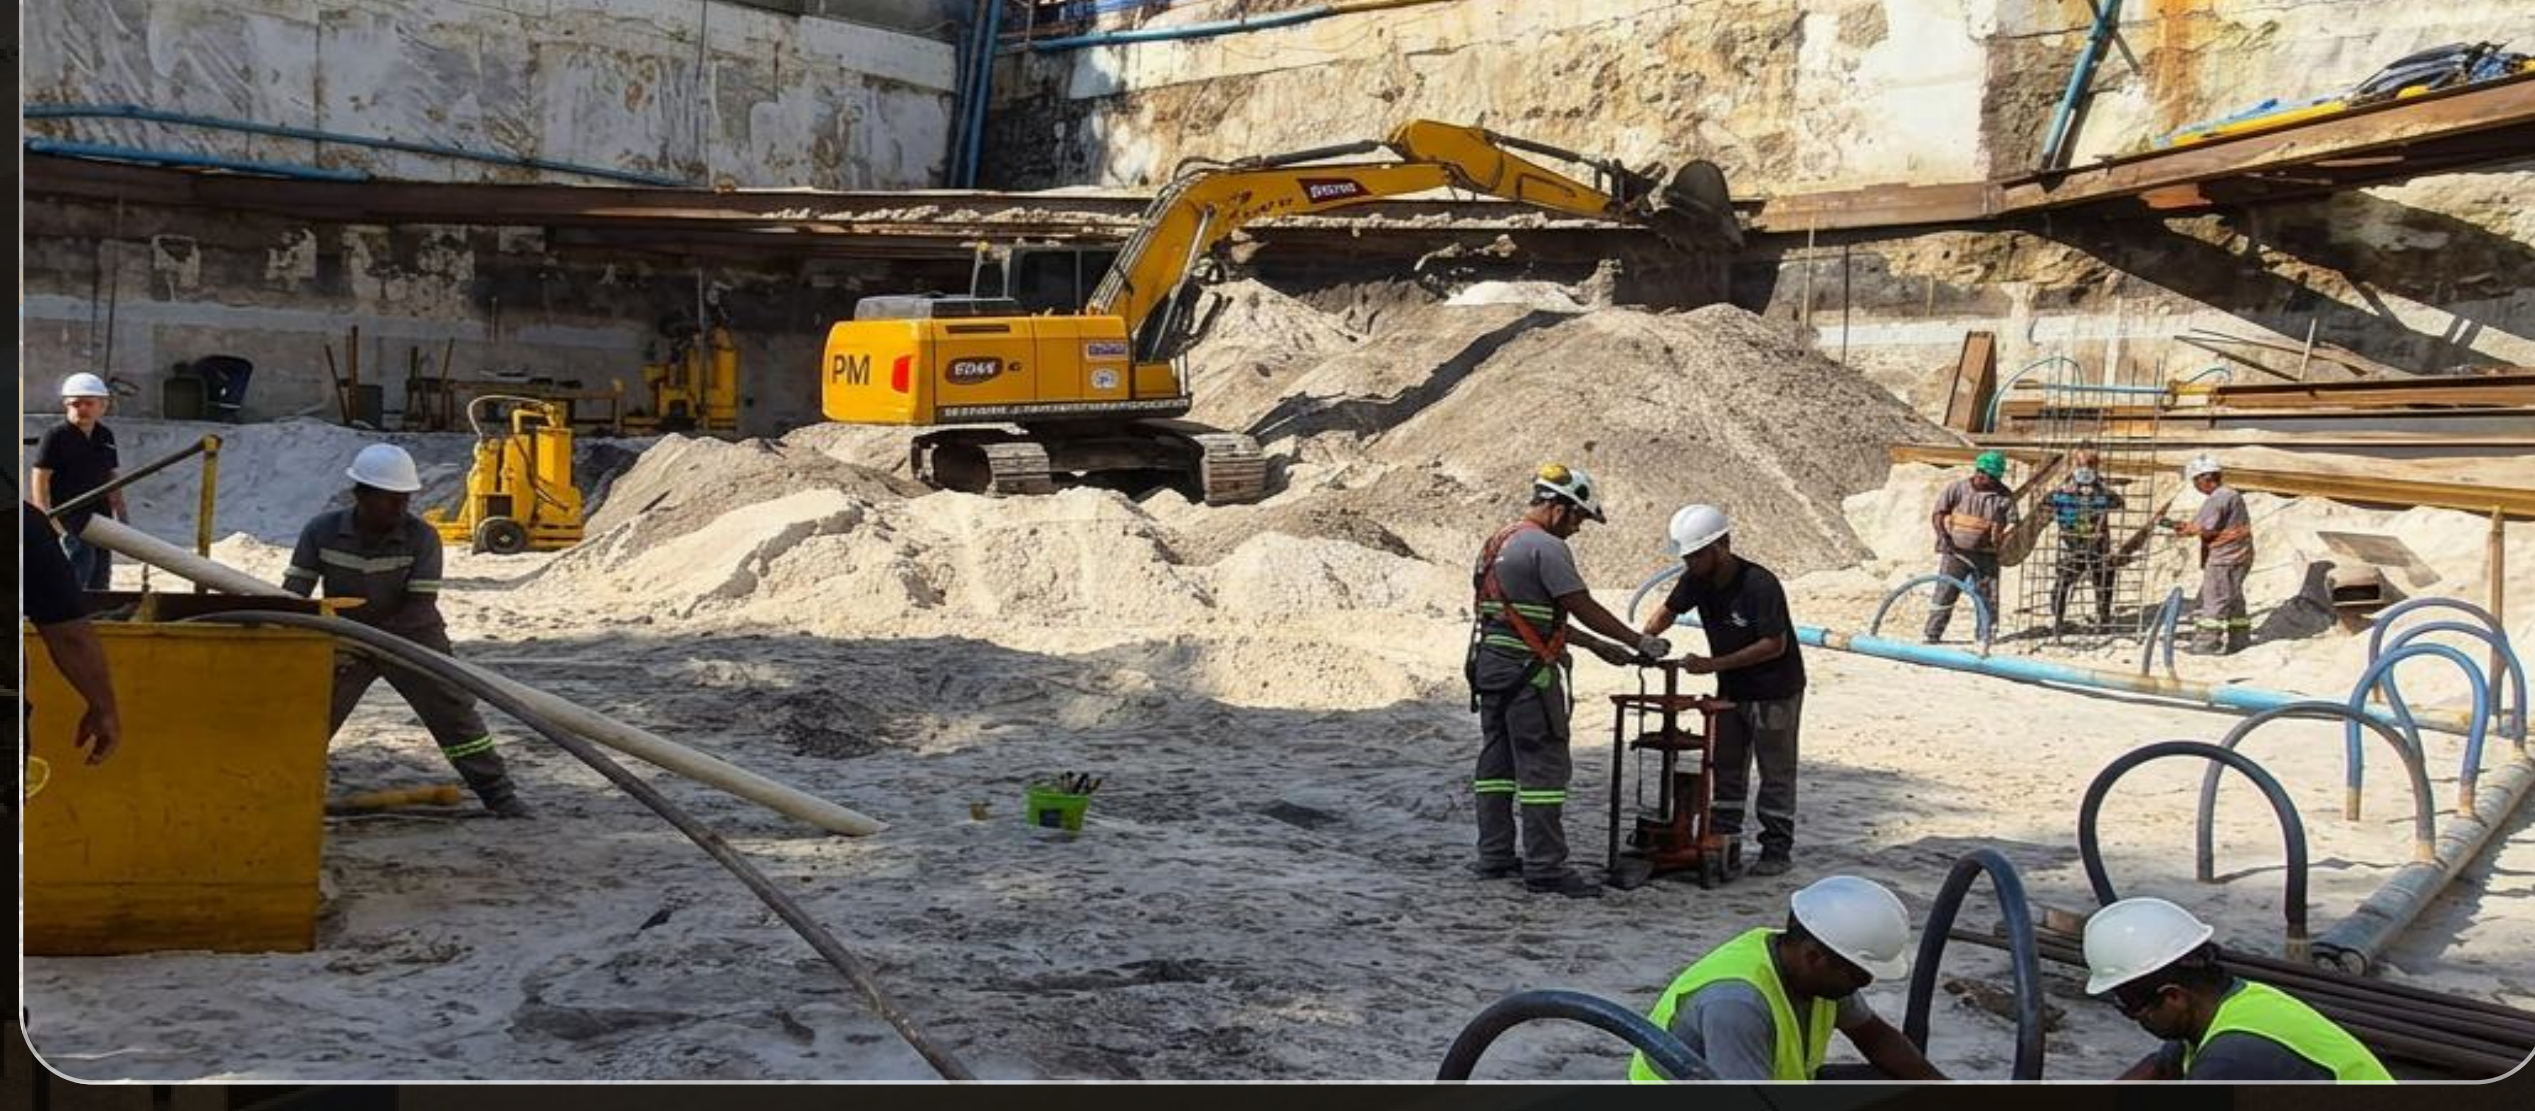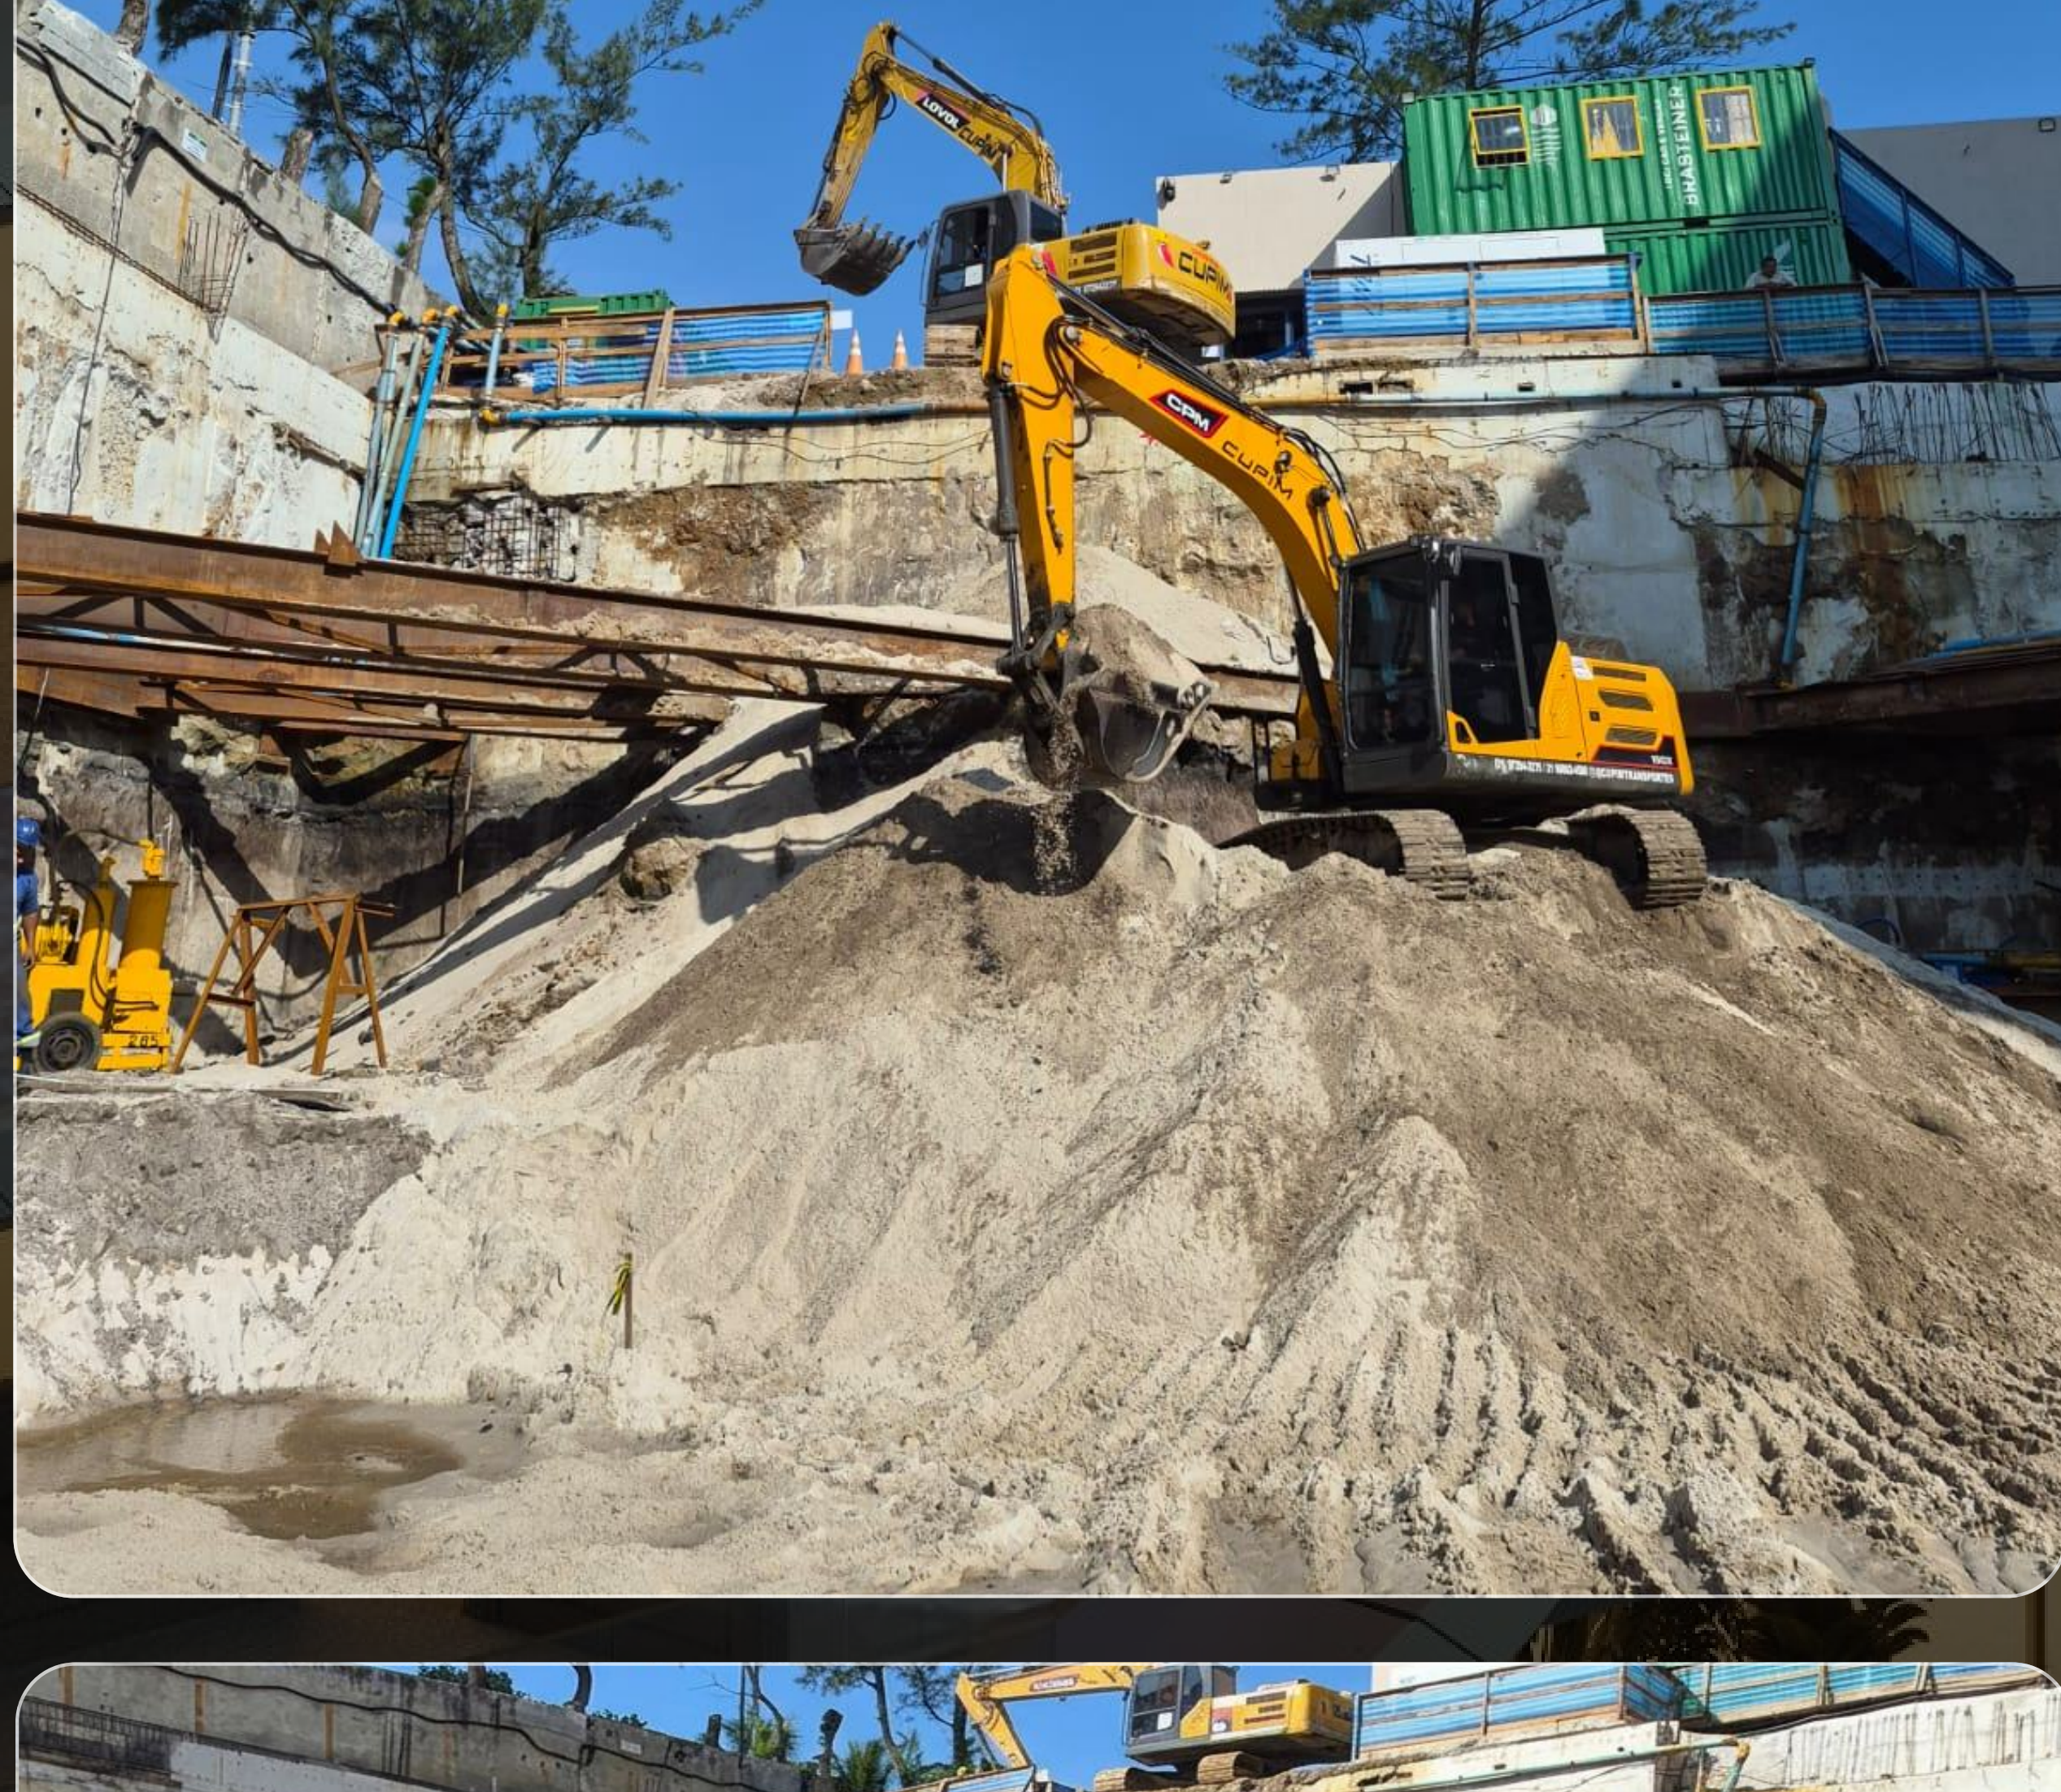

We also achieved important progress in the mechanical excavation, bringing the project closer to the start of the foundation footing execution cycle.

In parallel, we advanced the dewatering of the water table and maintained continuous monitoring of the shoring systems, ensuring safety and control throughout the execution of the work.

We continue moving forward, within the schedule, with safety and consistency, preparing the project for the next stages of the development.

MILESTONES

Estimated Occupancy Permit	25/11/2027
Estimated Condominium Installation Meeting	24/01/2028

ACTIVITY HISTOGRAM



MOBILIZATION

100%



DEMOLITION

100%



SHORING AND FOUNDATIONS

53%



STRUCTURE

1%



MASONRY

0%



CLADDINGS / WALL & FLOOR FINISHES

0%



FINAL FINISHES

0%

ACOMPANHAMENTO DE OBRA



RIO DE JANEIRO - RJ

[Watch the last update timelapse](#)
